Incor Lake City – Hyderabad

Jun’26 Fortnight – 1 Progress (01 Jun’26 to 15 Jun’26)

Road Works :

Week-1:

Entrance road WMM layer leveling chainage 100 to 185 WIP

Entrance road WMM compaction WIP

Week-2:

Entrance road WMM layer leveling chainage 100 to 185 WIP

100 to 230m chainage entrance road compaction WIP

Side drains :

Week-1:

Entrance road drain slab steel binding WIP

Entrance road drain slab side shuttering WIP

Week-2:

Entrance road West side drain Slab reinforcement tying WIP

Entrance road west side drain slab casting in progress at 5m to 65m

Curved wall :

Week-1:

Curved wall fountain area soil dressing WIP

Curved wall fountain grade slab reinforcement WIP

Week-2:

Curve wall fountain grade slab completed & brickwork WIP

Curved wall Putty work & fountain area brick work completed

Compound wall :

Fortnight- 1:

Compound wall soil excavation WIP

Compound wall PCC laying WIP

Compound wall raft & wall marking WIP

STP :

Week-1:

STP, Ramp area brickbat filling WIP

STP, Ramp area brickbat filling WIP

Week-2:

STP, Ramp area brickbat filling WIP

STP, Ramp area brickbat filling work completed

STP internal work :

Week-1:

STP, under the decant water tank, debris removal WIP

STP, Under the Decent water tank debris removal and cleaning WIP

Week-2:

STP, Treated water tank walls protection plaster WIP

STP, Treated water tank walls protection plaster work completed

Lift lobby:

Week-1:

Lift Lobby -01, Passenger Lift No-04, fin wall, 13th floor to 17th floor brick WIP

LL - 02 , B - 2 Level , lift pit - 8 1&2nd coat waterproofing completed

Week-2:

Tower -A 2nd floor Lift wall cutting WIP

Lift lobby no- 01, passenger lift pit no- 05, debris removal WIP

Lift Internal works :

Week-1:

L09 lift shaft Earth strip laying WIP

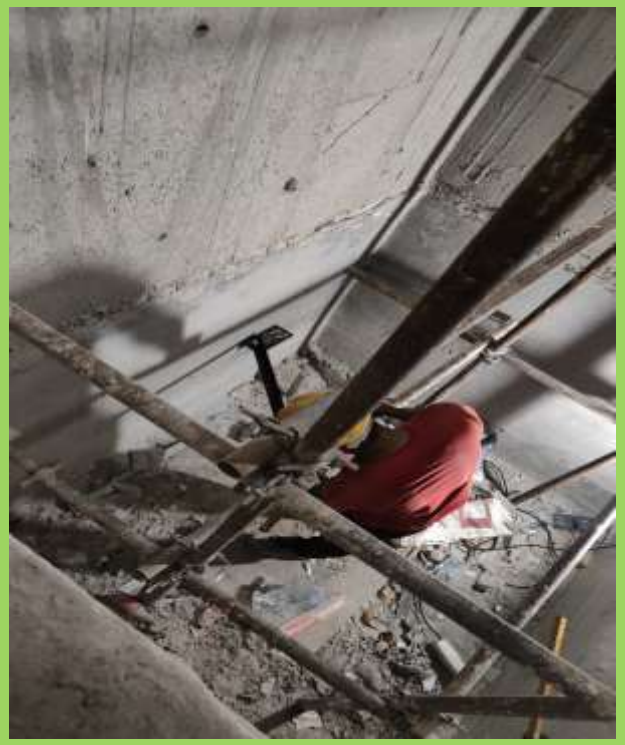

Basement -2 lift-9 bracket fixing WIP

Week-2:

L09 lift shaft Electrical work completed

Lift-8 Scaffolding installation works completed

Grade slab:

Week-1:

T-A B-2 grade slab Reinforcement WIP

T-A B-2 Grade slab north side casting WIP

Week-2:

T-A, B2 level grade slab purpose soil filling and leveling WIP at under ramp area (North East) side

Compound wall front side leveling WIP

T-A Basement :

Week-1:

Basement -2 GI pulling in progress

Basement-1 electrical room concrete work completed

Week-2:

T-A Basement - 1 Electrical panel room block work layout WIP

Basement - 1 Electrical panel room block WIP

Windows :

Week-1:

8th floor UPVC windows installation WIP

8th floor UPVC windows installation WIP

Week-2:

8th floor UPVC windows installation WIP

8th floor 1 to 17 flats UPVC windows installation completed

Flooring work :

Week-1:

Flat - 2131 toilet-01 wall dado WIP

Flat - 2131 toilet-01 & 02 wall dado & flooring completed

Week-2:

flat - 2133 toilet wall dado and flooring WIP

Flat – 2132 & 2133 toilet-01 wall dado & flooring completed

Corridor Flooring :

Week-1:

20th floor corridor tile flooring WIP

20th floor corridor tile flooring WIP

Week-2:

20th floor corridor tile flooring WIP

20th floor corridor tile flooring WIP

Painting Work :

Week-1:

Flat-722 sanding WIP

Flat-720 Sanding WIP

Week-2:

Flat – 2001 & 2003 1st coat fine putty completed

Flat – 725 , 726 & 729 primer completed

Plumbing work :

Fortnight – 1 :

Stilt floor PHE WIP

Tower -A 10th floor 20flat plumbing UPVC branch piping WIP

Tower -A plumbing shaft branch piping WIP

Electrical works :

Week-1:

Flat-1321 wiring WIP

Flat-1024 wiring WIP

Week-2:

23rd floor conduit WIP

1325,26 flats wiring WIP

Thank You

Incor Lake City – Hyderabad

Jun'26 Fortnight – 2 Progress (15 Jun'26 to 28 Jun'26)

Compound wall :

Week-1:

Compound wall raft marking WIP

Compound wall Raft concrete casting WIP

Week-2:

External compound wall reinforcement WIP

External compound wall concrete pouring WIP

Security cabin :

Week-1:

Security cabin pile excavation WIP

Security cabin plinth beam purpose soil leveling WIP

Week-2:

Security cabin plinth beam reinforcement tying WIP

Security cabin column shuttering WIP

Road Works :

Week-1:

Chainage 190m to 230m sub grade leveling WIP

Main road GSB leveling at chainage 190m to 220m

Week-2:

WMM leveling & compaction at chainage 10m to 150m

Main road DBM laying completed from 10m to 150m chainage

Drain Works :

Week-1:

Chainage 65m to 150m West side drain slab shuttering WIP

West side drain slab concreting upto chainage 150m WIP

Week-2:

East side drain slab concreting WIP at chainage 110m to 150m

Earthen ramp drain raft concrete pouring WIP

Doors :

Week-1:

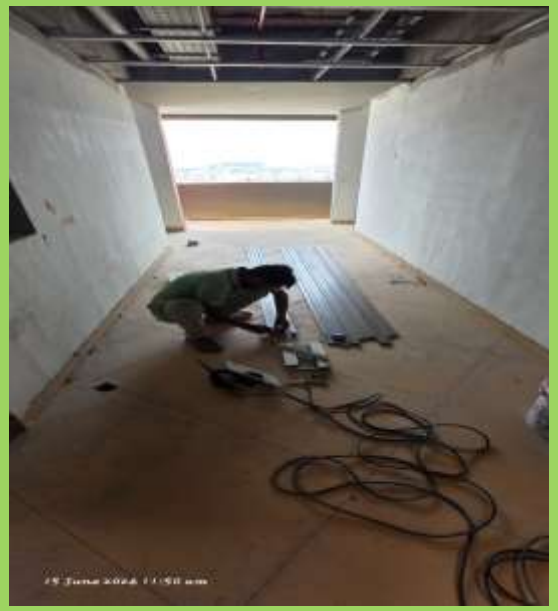

14th floor architrave WIP

12th floor shutters installation WIP

Week-2:

12th floor shutters installation WIP

12th floor anchor fasteners installation WIP

Windows :

Week-1:

7th floor UPVC windows installation WIP

7th floor UPVC windows installation WIP

Week-2:

7th floor UPVC Windows installation WIP

UPVC windows material shifting WIP for 6&7th floors

STP Internal works :

Fortnight - 2:

STP, Ultrafiltration tank walls surface preparation and rectification WIP

STP, Ultrafiltration tank walls, waterproofing protection plaster WIP

STP ultrafiltration tank and treated water tank cleaning WIP

Fire Fighting works :

Week-1:

Basement 1 fire fighting fabrication WIP

Basement 1 fire fighting MS pipe installation WIP

Week-2:

Basement 1 Fire fighting fabrication WIP

Basement 1 fire fighting MS pipe installation WIP

Painting works :

Week-1:

14th floor for pre primer touch up WIP

14 Floor Flats – 14 to 17 1st coat paint completed

Week-2:

Flat-1414 paint 1st coat WIP

Flats -1414 to 1417 paint 1st coat completed

Corridor flooring :

Week-1:

20th floor corridor skirting WIP

21st floor corridor flooring WIP

Week-2:

21st floor corridor main flooring WIP Near St-1&St-2 Area

21st floor corridor flooring up to ST-1&ST-2 completed

Main flooring :

Week-1:

22nd floor, in flat - 07, main flooring WIP

Flat - 2208, main flooring completed

Week-2:

22nd floor flat-05 Main flooring WIP

22nd floor flat-05 Main flooring completed

Electrical Works :

Fortnight – 2 :

Flat - 1327 ,1328 wiring and switch board fixing WIP

Flat - 1326 wiring WIP

Plumbing Works :

Week-1:

Flat - 2203 plumbing shaft work WIP

Plumbing shaft work UPVC branch piping WIP

Week-2:

Flat-28 Scaffolding installation for plumbing shaft WIP

Flat-28 Scaffolding works completed for plumbing shaft

Staircase Granite Works :

Fortnight - 2 :

Staircase-03, 20th floor to 22nd floor, granite flooring WIP

Staircase-03, 21st floor to 22nd floor, granite flooring WIP

Staircase-03, 22nd floor to 23rd floor, granite flooring WIP

Staircase-01, 19th floor to 21nd floor, granite flooring WIP

Lift Fin walls :

Week-1:

lift lobby - 01, 14th floor to 9th floor passenger lift - 08 & 10 , fin walls brick WIP

LL-01 2nd floor to 6th floor lift - 1,3&25 External face Lift – 04 internal & external face plastering

Week-2:

Lift lobby -1 18th floor service lift - 25 Lift -1&3,& 4 external plastering WIP

Lift lobby -2 lift -12 block work fin wall WIP

Lift Granite Works :

Week-1:

lift lobby - 01, 18th floor to 21st floor passenger lift - 04, and service lift - 25 Black pearl granite cladding WIP

Lift lobby - 01, 21st floor to terrace floor passenger lift - 03,04 & service lift - 25, Black pearl granite cladding WIP

Week-2:

Lift Lobby-1 Granite flooring laying WIP at the Stilt Floor

Lift lobby -1 lift-3&4 Service lift-25 threshold granite piece laying WIP

Electrical Room :

Week-1:

Basement-01 Electrical panel room block WIP

Basement-01 Electrical panel room block WIP

Week-2:

T-A stilt floor lift lobby-1 Screed concrete WIP

Stilt floor lift lobby -1 screed concrete laying Completed

RO Plant :

Week-1:

RO equipment arrived at site

RO equipment arrived

Week-2:

RO plant installation in progress

RO water installation completed

Basket ball & Pickel ball Court :

Fortnight – 2 :

Basket ball court Excavation WIP

Pickle ball court Excavation WIP

Pickel ball Court Excavation WIP

Thank You
